
Date:	03/24/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft):	145.6	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Byrd Fitzgerald	PSR:	P-902-015-017
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	e 34th ct		Flow Control:	Not Controlled	
City:	Hobart, IN		Year Renewed:		
Location:	Other		Tape/Media #:		
Purpose:	Not Known		Dia/Height:	10"	
Use:	Sanitary		Material:	VCP	
Drain Area:	NA		Lining:		
Category:	NA				
Comment:					
Location Details	:		Direction of Surve	y: Downstream	
US MH:	M-902-017	DS MH:	M-902-015	Total Length Surveyed (ft)	: <b>41.0</b>
D&M Index:	1.00	O&M Quick:	1700	O&M Rating:	7.00
Structural Index:	1.00	Structural Qu	uick: <b>1100</b>		1.00
Overall Index:	1.00	Overall Quic	1000	Overall Rating:	8.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-902-017

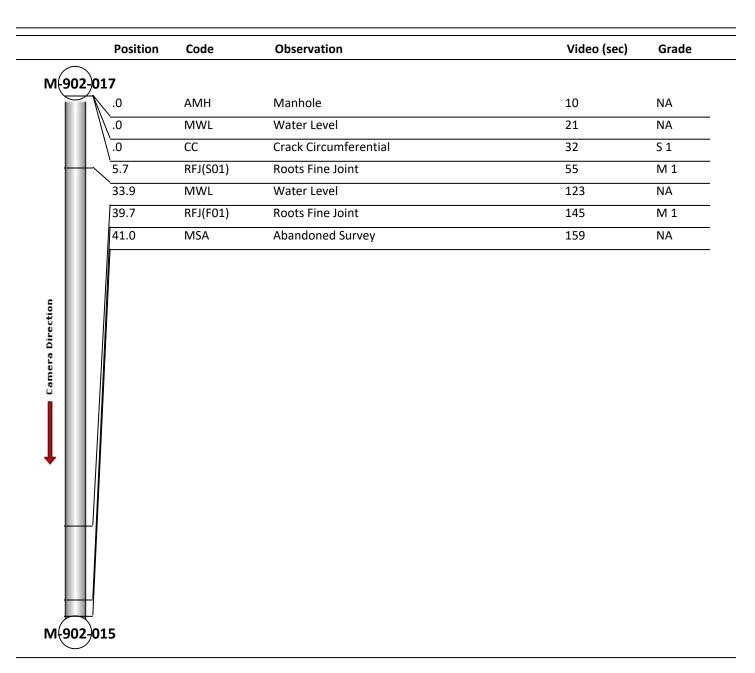

Code: MWL Description: Water Level

.0
0
0
5.000
NO



Code:	СС
Description:	Crack Circumferential

Distance (ft):	.0
Structural Grade:	1
O&M Grade:	0
Clock Start/From:	7
Clock To:	5
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:	RFJ
Description:	<b>Roots Fine Joint</b>
Distance (ft):	5.7
Structural Grade:	0
O&M Grade:	1
Clock Start/From:	7
Clock To:	5
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	S01

YES wandering

MWL

Water Level

Within 8" of Joint:

Remarks:

Code:

Description:



Distance (ft):	33.9
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	25.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	




Code:	RFJ
Description:	<b>Roots Fine Joint</b>
Distance (ft):	39.7
Structural Grade:	0
O&M Grade:	1
Clock Start/From:	7
Clock To:	5

1st Value: 2nd Value: Value Percent: Continuous Index: F01 Within 8" of Joint: YES Remarks: wanderin

wandering

Code: Description: MSA Abandoned Survey



Distance (ft):	41.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	stuck on joint/ debris
