Profile/Photo Observation Report



Date: 10/21/2021 Weather: **PACP 7.0** Coding: Pipe Length (ft): 319.0 Owner: **City of Hobart** Pre Clean: **Heavy Cleaning** P.O.#: YES502259 Surveyor: S. Bucklin PSR: P-503-077-076

Customer: City of Hobart Clean Date: 08/23/2021 Shape: C

Street: North Guyer Street Flow Control: Not Controlled

City: Hobart, IN Year Renewed: Location: Alley Tape/Media #:

Purpose: Routine Assessment Dia/Height: 10"
Use: Sanitary Sewage Pipe Material: VCP
Drain Area: Lining: None

Category: NA

Category. NA

Comment:

Location Details: Direction of Survey: **Upstream**

US MH: M-503-076 DS MH: M-503-077 Total Length Surveyed (ft): 138.1

1.96 3A24 53.00 O&M Index: O&M Quick: O&M Rating: 4.00 514B 72.00 Structural Quick: Structural Rating: Structural Index: 2.78 125.00 514B Overall Quick: Overall Rating: Overall Index:

	Position	Code	Observation	Video (sec)	Grade
M(503-	077				
\forall	0.	AMH	Manhole	1	NA
-11	0.	MWL	Miscellaneous Water Level	63	NA
-	\\\\ <u>.</u> 9	В	Broken	125	S 4
-11	.9	ISB	Infiltration Stain Barrel	157	M 1
	2.2	RTJ	Roots Tap Joint	205	M 2
- 11	\ \\6.7	RTJ	Roots Tap Joint	247	M 2
ш	6.7	FH4(S01)	Fracture Longitudinal Hinge, 4	272	S 4
-11	16.9	ISJ	Infiltration Stain Joint	341	M 1
	21.8	RFJ	Roots Fine Joint	408	M 1
s	21.9	DR	Deformed Rigid	422	S 5
Camera Direction	26.6	В	Broken	438	S 4
	\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\	DR	Deformed Rigid	458	S 4
nerg	29.6	В	Broken	473	S 4
Can	36.7	FH4(F01)	Fracture Longitudinal Hinge, 4	503	S 4
	46.4	B(S02)	Broken	554	S 4
	51.7	RMJ	Roots Medium Joint	595	M 3
	53.2	TFD	Tap Factory Defective	630	M 3
	¬\\\	RFJ	Roots Fine Joint	659	M 1
	54.0	B(F02)	Broken	672	S 4

\\ <u></u>	FS	Fracture Spiral	745	S 3
63.7	RFJ	Roots Fine Joint	803	M 1
78.9	RFJ	Roots Fine Joint	892	M 1
80.1	TFD	Tap Factory Defective	916	M 3
81.2	FM(S03)	Fracture Multiple	959	S 4
85.4	OBN	Obstruction Construction Debris	994	M 2
85.9	RFJ	Roots Fine Joint	1039	M 1
90.7	RMJ	Roots Medium Joint	1085	M 3
92.3	FM(F03)	Fracture Multiple	1123	S 4
105.8	RFJ	Roots Fine Joint	1203	M 1
105.8	ISJ	Infiltration Stain Joint	1236	M 1
// 110.8	RMJ(S04)	Roots Medium Joint	1277	M 3
$/\!/_{124.0}$	OBN	Obstruction Construction Debris	1354	M 3
/ 124.3	В	Broken	1432	S 4
124.3	ISB	Infiltration Stain Barrel	1459	M 1
130.0	В	Broken	1521	S 4
131.4	ISB	Infiltration Stain Barrel	1556	M 1
136.8	TFD	Tap Factory Defective	1627	M 3
137.4	RTJ	Roots Tap Joint	1661	M 2
<u> </u> 137.4	RMJ(F04)	Roots Medium Joint	1675	M 3
138.1	ISJ	Infiltration Stain Joint	1753	M 1
138.1	MSA	Miscellaneous Survey Abandoned	1782	NA


Code:

M 503-076



Description:	Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-503-07

 AMH

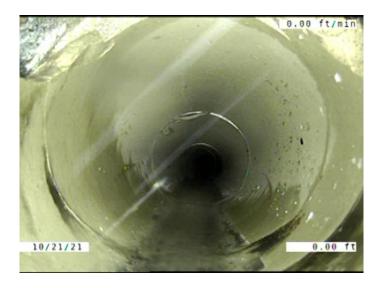

Code: MWL

Description: Miscellaneous Water Level

Distance (ft): .0
Structural Grade: 0
O&M Grade: 0

Clock Start/From:

Clock To: 1st Value: 2nd Value:


Value Percent: 5.000

Continuous Index:

Within 8" of Joint:

Remarks:

NO

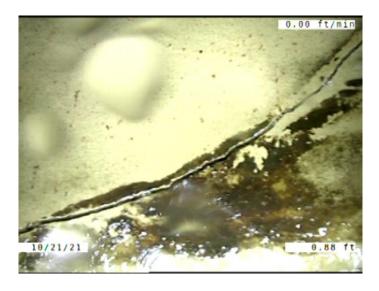

Code: B
Description: Broken

Distance (ft): .9
Structural Grade: 4
O&M Grade: 0
Clock Start/From: 12
Clock To: 12
1st Value:
2nd Value:
Value Percent:
Continuous Index:

Remarks:

Within 8" of Joint:

YES




Code: ISB
Description: Infiltration Stain Barrel

Distance (ft): .9
Structural Grade: 0
O&M Grade: 1
Clock Start/From: 3
Clock To: 9
1st Value:
2nd Value:
Value Percent:
Continuous Index:

Within 8" of Joint:

Remarks:

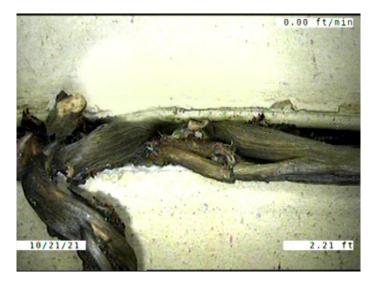

Code: RTJ

Description: Roots Tap Joint

YES

Distance (ft): 2.2
Structural Grade: 0
O&M Grade: 2
Clock Start/From: 10
Clock To: 1
1st Value:
2nd Value:

Value Percent: 5.000

Continuous Index:

Within 8" of Joint: YES



Code: RTJ

Description: Roots Tap Joint

Distance (ft): 6.7
Structural Grade: 0
O&M Grade: 2
Clock Start/From: 11

Clock To: 1st Value: 2nd Value:


Value Percent: 5.000

Continuous Index:

Within 8" of Joint:

Remarks:

YES

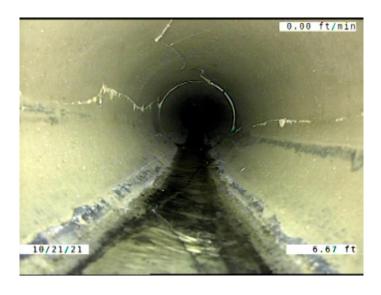

Code: FH4

Description: Fracture Longitudinal Hinge, 4

Distance (ft): 6.7
Structural Grade: 4

O&M Grade: 0

Clock Start/From: 12

Clock To: 12

1st Value: 2nd Value: Value Percent:

Continuous Index: **S01** Within 8" of Joint: **YES**



Code: ISJ

Description: Infiltration Stain Joint


Distance (ft): 16.9
Structural Grade: 0
O&M Grade: 1
Clock Start/From: 2
Clock To: 5

1st Value: 2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

YES

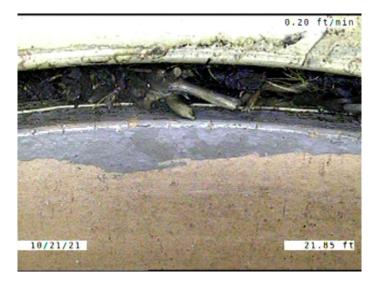

Code: RFJ

Description: Roots Fine Joint

Distance (ft):

Structural Grade:

O&M Grade:

Clock Start/From:

Clock To:

1st Value:

2nd Value:

Value Percent:

Continuous Index:

Within 8" of Joint: YES



Code: DR

Description: Deformed Rigid

Distance (ft): 21.9
Structural Grade: 5
O&M Grade: 0

Clock Start/From:

Clock To: 1st Value: 2nd Value:


Value Percent: 10.000

Continuous Index:

Within 8" of Joint:

Remarks:

NO

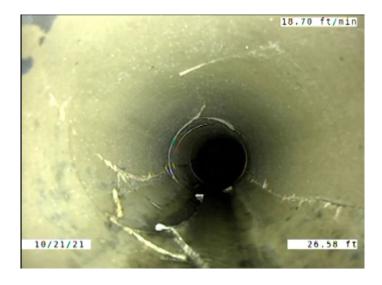

Code: **B**

Description: Broken

Distance (ft): 26.6
Structural Grade: 4
O&M Grade: 0
Clock Start/From: 6
Clock To: 8
1st Value:

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: NO



Code: DR

Description: **Deformed Rigid**

Distance (ft): 27.5
Structural Grade: 4
O&M Grade: 0

Clock Start/From:

Clock To: 1st Value: 2nd Value:


Value Percent: 5.000

Continuous Index:

Within 8" of Joint:

Remarks:

NO

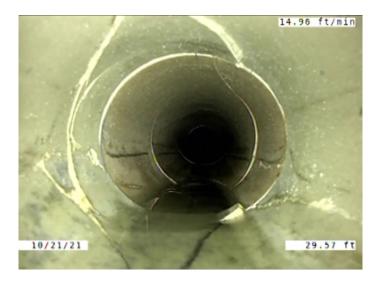

Code: **B**

Description: Broken

Distance (ft): 29.6
Structural Grade: 4


O&M Grade: 0

Clock Start/From: 12

Clock To: 12
1st Value:
2nd Value:

Value Percent: Continuous Index:

Within 8" of Joint: YES

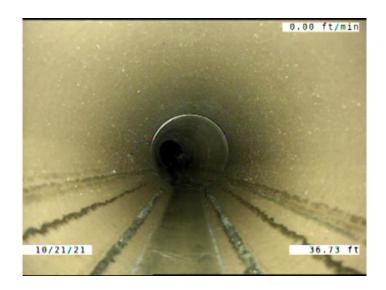

Code: FH4

Description: Fracture Longitudinal Hinge, 4

Distance (ft): 36.7
Structural Grade: 4

O&M Grade: 0

Clock Start/From: 12


Clock To: 12

1st Value:

2nd Value:

Value Percent:
Continuous Index: F01
Within 8" of Joint: YES

Remarks:

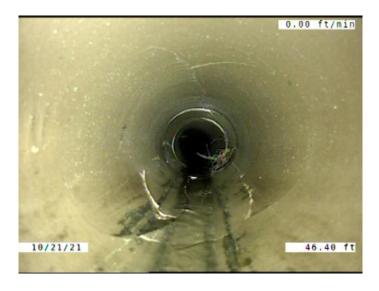

Code: **B**

Description: Broken

Distance (ft): 46.4
Structural Grade: 4

O&M Grade: 0

Clock Start/From: 12

Clock To: 12

1st Value:
2nd Value:

Continuous Index: **S02** Within 8" of Joint: **YES**

Remarks:

Value Percent:



Code: RMJ

Description: Roots Medium Joint

Distance (ft): 51.7
Structural Grade: 0

O&M Grade: 3

Clock Start/From: 2

Clock To: 5

1st Value: 2nd Value:

Value Percent: 5.000

Continuous Index:

Within 8" of Joint:

Remarks:

YES



Code: **TFD**

Description: Tap Factory Defective

Distance (ft): 53.2
Structural Grade: 0
O&M Grade: 3
Clock Start/From: 1


Clock To:

1st Value: **4.000**

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: YES

Remarks: **Defective**

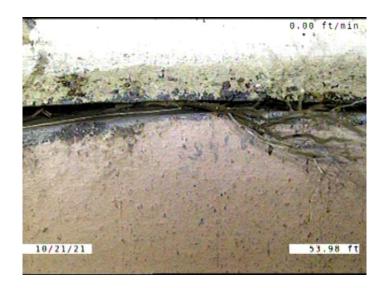

Code: RFJ
Description: Roots Fine Joint


Distance (ft): 54.0 Structural Grade: 0 O&M Grade: 1 Clock Start/From: 8 Clock To: 10 1st Value: 2nd Value: Value Percent: Continuous Index: Within 8" of Joint: YES

Remarks:



Code: B
Description: Broken

Distance (ft): 54.0 Structural Grade: 4 O&M Grade: 0 Clock Start/From: 12 Clock To: 12 1st Value: 2nd Value: Value Percent: Continuous Index: F02 Within 8" of Joint: YES

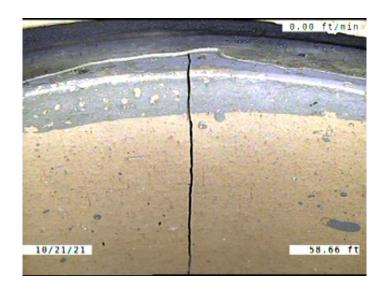

Code: **FS**

Description: Fracture Spiral

Distance (ft): 58.7
Structural Grade: 3
O&M Grade: 0
Clock Start/From: 12
Clock To: 1

1st Value: 2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: YES

Remarks:



Code: RFJ

Description: Roots Fine Joint

Distance (ft): 63.7 Structural Grade: 0 O&M Grade: 1 Clock Start/From: 8 Clock To: 4 1st Value: 2nd Value: Value Percent: Continuous Index: Within 8" of Joint: YES



Code: RFJ

Description: Roots Fine Joint

Distance (ft): 78.9
Structural Grade: 0
O&M Grade: 1
Clock Start/From: 10
Clock To: 2

1st Value: 2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

YES



Code: **TFD**

Description: Tap Factory Defective

Distance (ft): 80.1
Structural Grade: 0

O&M Grade: 3

Clock Start/From: 10

Clock To:

1st Value: **4.000**

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: YES

Remarks: **Defective**



Code: FM

Description: Fracture Multiple

Distance (ft): 81.2
Structural Grade: 4

O&M Grade: 0

Clock Start/From: 12

Clock To: 12

1st Value: 2nd Value: Value Percent:

Continuous Index: **S03**Within 8" of Joint: **YES**

Remarks:



Code: OBN

Description: Obstruction Construction Debris

Distance (ft): 85.4
Structural Grade: 0

O&M Grade: 2

Clock Start/From: 6

Clock To: 7

1st Value: 2

2nd Value:

Value Percent: 5.000

Continuous Index:

Within 8" of Joint: YES



Code: RFJ

Description: Roots Fine Joint

Distance (ft): 85.9
Structural Grade: 0

O&M Grade: 1

Clock Start/From: 10


Clock To: 2

1st Value: 2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

YES

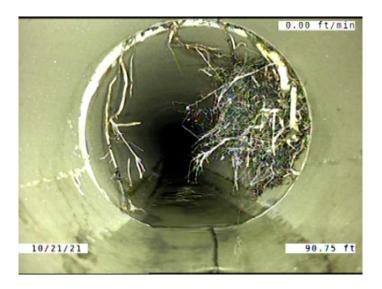

Code: RMJ

Description: Roots Medium Joint

Distance (ft): 90.7
Structural Grade: 0

O&M Grade: 3

Clock Start/From: 10

Clock To: 4

1st Value:

2nd Value: Value Percent:

alue Percent: 15.000

Continuous Index:

Within 8" of Joint: YES



Code: FM
Description: Fracture Multiple

Distance (ft): 92.3
Structural Grade: 4
O&M Grade: 0
Clock Start/From: 12
Clock To: 12
1st Value:

1st Value: 2nd Value: Value Percent:

Continuous Index: F03
Within 8" of Joint: YES

Remarks:


Remarks:



Code: RFJ

Description: Roots Fine Joint

Distance (ft): 105.8 Structural Grade: 0 O&M Grade: 1 Clock Start/From: 10 3 Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index: Within 8" of Joint: YES

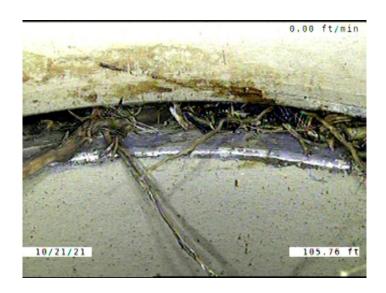

Code: ISJ

Description: Infiltration Stain Joint


Distance (ft): 105.8
Structural Grade: 0
O&M Grade: 1
Clock Start/From: 8
Clock To: 1

1st Value: 2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

YES

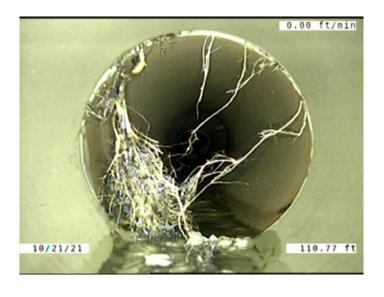

Code: RMJ

Description: Roots Medium Joint

Distance (ft): 110.8
Structural Grade: 0
O&M Grade: 3
Clock Start/From: 7
Clock To: 3
1st Value:

2nd Value:
Value Percent: 10.000
Continuous Index: \$04
Within 8" of Joint: YES



Code: OBN

Description: Obstruction Construction Debris

Distance (ft): 124.0
Structural Grade: 0
O&M Grade: 3
Clock Start/From: 5
Clock To: 7


1st Value: 2nd Value:

Value Percent: 15.000

Continuous Index:

Within 8" of Joint: YES

Remarks:

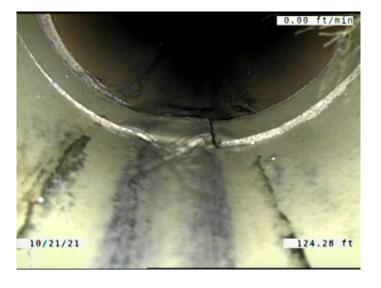

Code: B

Description: Broken


Distance (ft): 124.3
Structural Grade: 4

O&M Grade: 0
Clock Start/From: 2

Clock To: 9
1st Value:

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: YES

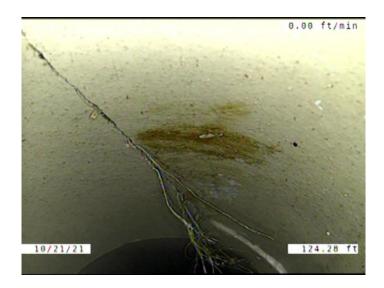

Code: ISB

Description: Infiltration Stain Barrel

Distance (ft): 124.3
Structural Grade: 0
O&M Grade: 1
Clock Start/From: 3
Clock To: 4
1st Value:
2nd Value:
Value Percent:
Continuous Index:

Within 8" of Joint:

Remarks:

Code:

0.00 ft/min

В

YES

Description: Broken

Distance (ft): 130.0
Structural Grade: 4
O&M Grade: 0
Clock Start/From: 12
Clock To: 12
1st Value:
2nd Value:

Value Percent: Continuous Index:

Within 8" of Joint: YES



Code: ISB

Description: Infiltration Stain Barrel

Distance (ft): 131.4
Structural Grade: 0
O&M Grade: 1
Clock Start/From: 3
Clock To: 5

1st Value: 2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

NO



Code: **TFD**

Description: Tap Factory Defective

Distance (ft): 136.8
Structural Grade: 0
O&M Grade: 3
Clock Start/From: 2


Clock To:

1st Value: **4.000**

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: YES

Remarks: **Defective**

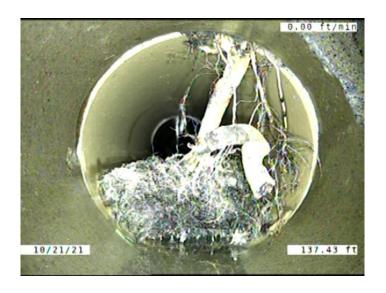

Code: RTJ

Description: Roots Tap Joint

Distance (ft): 137.4
Structural Grade: 0
O&M Grade: 2
Clock Start/From: 12
Clock To: 8

1st Value: 2nd Value:

Value Percent: 35.000

Continuous Index:

Within 8" of Joint:

Remarks:

Code:

0.00 ft/min


137.43 ft



Description: Roots Medium Joint

YES

RMJ




1st Value: 2nd Value:

Value Percent: 10.000
Continuous Index: F04
Within 8" of Joint: YES

Remarks:



10/21/21

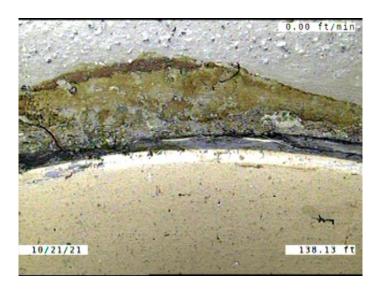

Code: ISJ

Description: Infiltration Stain Joint


Distance (ft): 138.1
Structural Grade: 0
O&M Grade: 1
Clock Start/From: 9
Clock To: 11

1st Value:
2nd Value:
Value Percent:
Continuous Index:

Within 8" of Joint:

Remarks:

YES

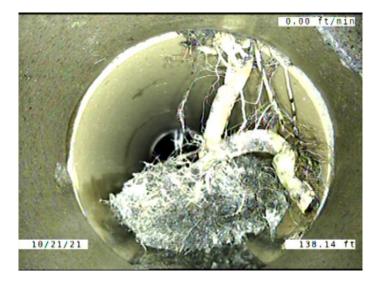

Code: MSA

Description: Miscellaneous Survey Abandoned

Distance (ft): 138.1
Structural Grade: 0

O&M Grade: 0

Clock Start/From:

Clock To:
1st Value:
2nd Value:
Value Percent:
Continuous Index:

Within 8" of Joint: NO

Remarks: CAMERA CANT MAKE IT PAST TAP

ROOT
