Profile/Photo Observation Report



Date: 10/01/2018 Weather: **PACP 6.0** Coding: Pipe Length (ft): 209.4 Owner: NA Pre Clean: **Not Known** P.O.#: **Michael Carlino** PSR: P-803-016-015 Surveyor:

Customer: Clean Date: 01/01/1900 Shape: C

Street: 40th. Ave. Flow Control: Not Controlled

City: Hobart, IN Year Renewed:
Location: Light Highway Tape/Media #:

Purpose: Routine Assessment Dia/Height: 12"
Use: Sanitary Material: VCP

Drain Area: NA Lining:

Category: NA

Comment:

Location Details: Direction of Survey: **Upstream**


US MH: M-803-015 DS MH: M-803-016 Total Length Surveyed (ft): 29.7

2.38 5133 19.00 O&M Index: O&M Quick: O&M Rating: 0.00 0000 0.00 Structural Quick: Structural Rating: Structural Index: 2.38 5133 19.00 Overall Quick: Overall Rating: Overall Index:

Po	sition Co	ode	Observation	Video (sec)	Grade
803-016					
0.	AN	Л Н I	Manhole	10	NA
0.	M	WL '	Water Level	20	NA
5.1	. RF	J I	Roots Fine Joint	41	M 1
7.9	RN	/IJ I	Roots Medium Joint	57	M 3
/ 10.	7 RN	/IJ I	Roots Medium Joint	73	M 3
//14.	0 RF	J	Roots Fine Joint	90	M 1
 / 20.	4 TF	D -	Tap Factory Defective	114	M 2
20.	4 RF	L	Roots Fine Lateral	124	M 1
/ 25.	8 RN	/IJ I	Roots Medium Joint	146	M 3
28.	7 RB	BB I	Roots Ball Barrel	163	M 5
29.	.7 MS	SA ,	Abandoned Survey	176	NA
\mathbb{H}					



Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-803-016

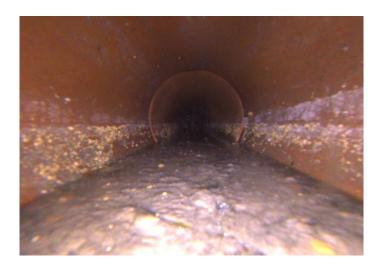

Code: MWL Description: **Water Level**

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From:

Clock To: 1st Value: 2nd Value:

Value Percent: 20.000

Continuous Index:

Within 8" of Joint:

Remarks:

NO



Code: RFJ

Description: **Roots Fine Joint**

Distance (ft): 5.1 Structural Grade: 0 O&M Grade: 1 Clock Start/From: 9 Clock To: 1 1st Value: 2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

YES



Code: RMJ

Description: **Roots Medium Joint**

Distance (ft): 7.9 Structural Grade: 0 3 O&M Grade: Clock Start/From: 9 Clock To: 4

1st Value: 2nd Value:

Value Percent: 25.000

Continuous Index:

Within 8" of Joint:

Remarks:

YES



Code: RMJ

Description: **Roots Medium Joint**

Distance (ft): 10.7 Structural Grade: 0 O&M Grade: 3 Clock Start/From: 9 3 Clock To: 1st Value:

30.000 Value Percent:

Continuous Index:

Within 8" of Joint:

Remarks:

2nd Value:

YES



Code: RFJ

Description: Roots Fine Joint

Distance (ft): 14.0
Structural Grade: 0
O&M Grade: 1
Clock Start/From: 10
Clock To: 2
1st Value:

1st Value: 2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

YES



Code: **TFD**

Description: Tap Factory Defective

Distance (ft): 20.4
Structural Grade: 0

O&M Grade: 2

Clock Start/From: 2


Clock To:

2nd Value:

1st Value: **6.000**

Value Percent: Continuous Index:

Within 8" of Joint: NO Remarks: RFL

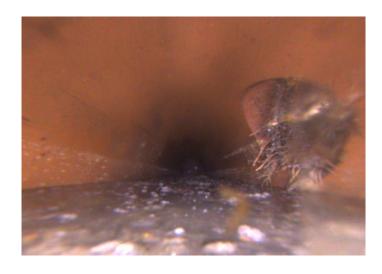

Code: RFL

Description: Roots Fine Lateral

Distance (ft): 20.4
Structural Grade: 0

O&M Grade: 1


Clock Start/From: 2

Clock To:
1st Value:
2nd Value:
Value Percent:
Continuous Index:

Within 8" of Joint:

Remarks:

NO

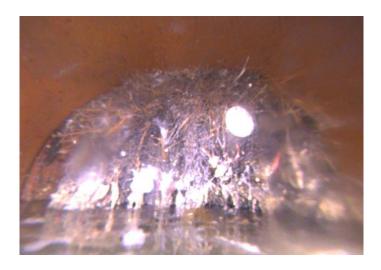

Code: RMJ

Description: Roots Medium Joint

Distance (ft): 25.8
Structural Grade: 0

O&M Grade: 3

Clock Start/From: 9

Clock To: 3

1st Value:

Value Percent: 25.000


Continuous Index:

Within 8" of Joint:

Remarks:

2nd Value:

YES

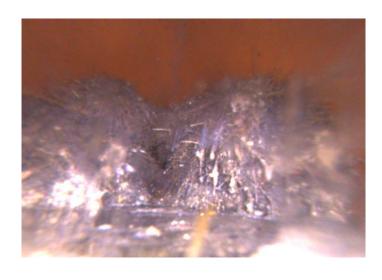

Code: RBB

Description: Roots Ball Barrel

Distance (ft): 28.7
Structural Grade: 0

O&M Grade: 5

Clock Start/From: 9

Clock To: 3

1st Value: 2nd Value:

Value Percent: 85.000

Continuous Index:

Within 8" of Joint:

Remarks:

NO



Code: MSA

Description: Abandoned Survey

Distance (ft): 29.7
Structural Grade: 0

O&M Grade: 0

Clock Start/From:

Clock Start/Ti

Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: NO Remarks: RBB
