

Date: Pipe Length (fi	10/23/2021	Weather: Owner:	Hobart, IN	Coding: Pre Clean:	PACP 6.0 Not Known
P.O.#:	994_1	Surveyor:	M. Pielacha	PSR:	P-303-007-006
Customer:	– Hobart, IN	Clean Date:		Shape:	с
Street:	Off Old Ridge Road		Flow Control:		
City:	Hobart, IN		Year Renewed:		
Location:	Sidewalk		Tape/Media #:	994	
Purpose:	Routine Assessmen	t	Dia/Height:	12"	
Use:	Sanitary		Material:	VCP	
Drain Area:			Lining:		
Category:	NA				
Comment:					
Location Detai	ils:		Direction of Surve	ey: Upstream	
US MH:	M-303-7	DS MH:	M-303-6	Total Length Surveyed (ft)	: 62 .9
D&M Index:	2.50	O&M Quick:	3222	O&M Rating:	10.00
Structural Index	. 0.00	Structural Qu	ick: 0000		0.00
Overall Index:	2.50	Overall Quick		Ŭ	10.00



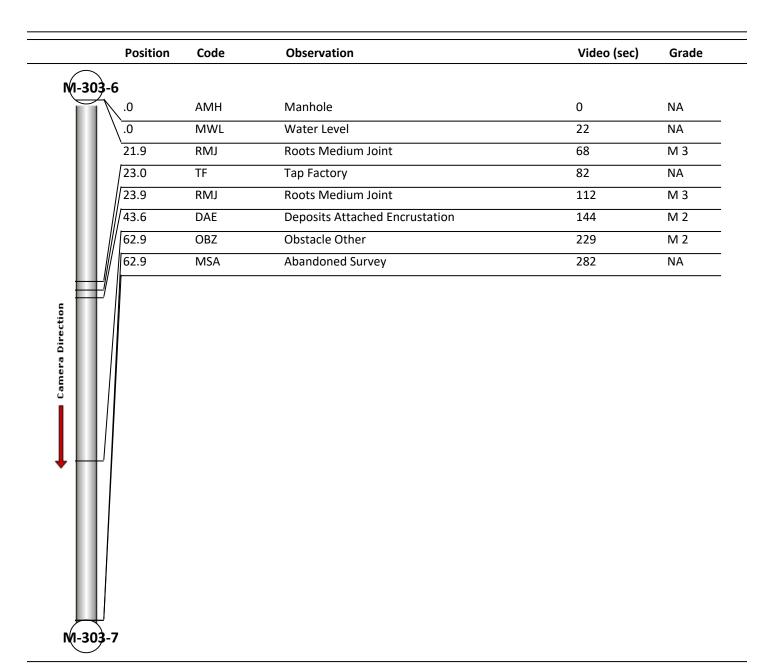

Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-303-6

Thursday, May 4, 2023

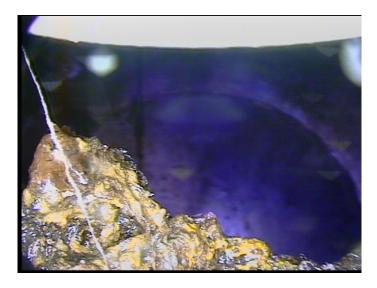

Code:	MWL
Description:	Water Level
	•
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	RMJ Roots Medium Joint
Distance (ft):	21.9
Structural Grade:	0
O&M Grade:	3
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Code:	TF
Description:	Tap Factory
Distance (ft):	23.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	2
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	RMJ Roots Medium Joint
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index: Within 8" of Joint: Remarks:	23.9 0 3 10 12 5.000 YES
Nethalks.	




Code: Description:	DAE Deposits Attached Encrustation
Distance (ft):	43.6
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	7
Clock To:	5
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	
Within 8" of Joint:	YES

Remarks:



Code: Description:	OBZ Obstacle Other
Distance (ft):	62.9
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	4
Clock To:	8
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	under water debris

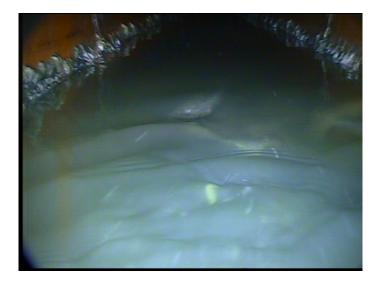

Code: Description:	MSA Abandoned Survey
Distance (ft):	62.9
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	under water debris
