# Manhole Inspection Report

| | | | | | |
|---|---|---|---|---|---|
| Date: | **05/16/2018** | Weather: | | Coding: | **RZMACP** |
| MH#: | **M-704-018** | Owner: | **NA** | Len. Surveyed: | **5.3** |
| P.O.#: | | Surveyor: | **Jen Costello** | Rim to Invert: | **6.3** |
| Customer: | | Cert. #: | **U-907-5518** | Wall Material: | **Brick** |

| | | | |
|---|---|---|---|
| Street: | **Michigan Ave. 736' South of South S** | Project: | **Hobart, IN** |
| City: | **Hobart, IN** | GPS Northing: | **2906687.008** |
| Location: | | GPS Easting: | **2906687.008** |
| Drain Area: | **Northeast** | GPS Accuracy: | **Sub-Meter** |
| Cover Shape: | **Circular** | Evidence of Surcharge: | **No** |
| Cover Size: | **22.5** | Potential for Runoff: | **None** |
| Comments: | | | |

| | | | | | |
|---|---|---|---|---|---|
| O&M Index: | **2.00** | O&M Quick: | **2100** | O&M Rating: | **2.00** |
| Structural Index: | **3.00** | Structural Quick: | **3100** | Structural Rating: | **3.00** |
| Overall Index: | **2.50** | Overall Quick: | **3121** | Overall Rating: | **5.00** |

| Position | Code | Observation | Video (sec) | Grade |
|---|---|---|---|---|
| **M-704-018** | | | | |
| .0 | DB | Displaced Brick | 10 | S 3 |
| .0 | MGO | General Observation | 21 | NA |
| 1.9 | MGO | General Observation | 39 | NA |
| 4.5 | DSF | Deposits Settled Fine | 57 | M 2 |
| 5.3 | MGO | General Observation | 70 | NA |



Code: **DB**
Description: **Displaced Brick**

Distance (ft): **.0**
Structural Grade: **3**
O&M Grade: **0**
Clock Start/From: **12**
Clock To: **12**
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks:

| | |
|---|---|
| Code: | **MGO** |
| Description: | **General Observation** |
| Distance (ft): | **.0** |
| Structural Grade: | **0** |
| O&M Grade: | **0** |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | |
| Step: | **NO** |
| Remarks: | **ACCESS MH** |

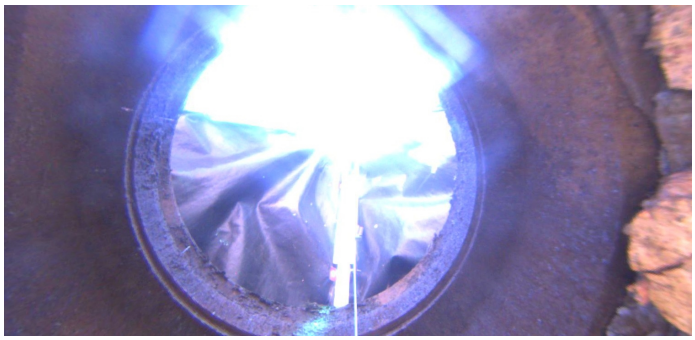

| | |
|---|---|
| Code: | **MGO** |
| Description: | **General Observation** |
| Distance (ft): | **1.9** |
| Structural Grade: | **0** |
| O&M Grade: | **0** |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | |
| Step: | **NO** |
| Remarks: | **END SURVEY** |

| | |
|---|---|
| Code: | **DSF** |
| Description: | **Deposits Settled Fine** |
| Distance (ft): | **4.5** |
| Structural Grade: | **0** |
| O&M Grade: | **2** |
| Clock Start/From: | **12** |
| Clock To: | **12** |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | **5.000** |
| Step: | **NO** |
| Remarks: | |

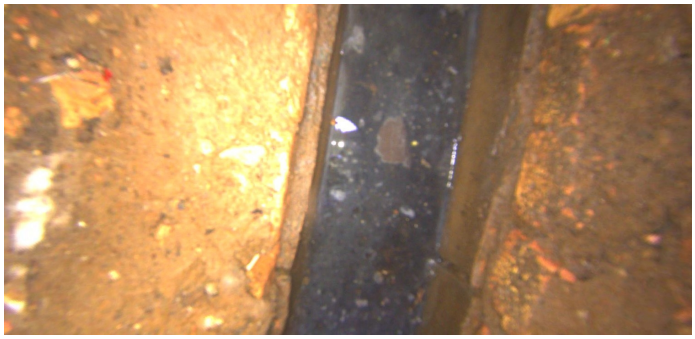

| | |
|---|---|
| Code: | **MGO** |
| Description: | **General Observation** |
| Distance (ft): | **5.3** |
| Structural Grade: | **0** |
| O&M Grade: | **0** |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | |
| Step: | **NO** |
| Remarks: | **END SURVEY** |
