Manhole Inspection Report

Date:	**04/24/2018**	Weather:		Coding:	**RZMACP**
MH#:	**M-707-033**	Owner:	**NA**	Len. Surveyed:	**7.0**
P.O.#:		Surveyor:	**John Kuglmaier**	Rim to Invert:	**6.7**
Customer:	**8.7**	Cert. #:	**U-1215-07002349**	Wall Material:	**Brick**

Street:	**Lincoln St. 237' South of 10th St.**	Project:	**Hobart, IN**
City:	**Hobart, IN**	GPS Northing:	**0.0**
Location:		GPS Easting:	**0.0**
Drain Area:	**Southeast**	GPS Accuracy:	**Nearest Meter**
Cover Shape:	**Circular**	Evidence of Surcharge:	**No**
Cover Size:	**22.5**	Potential for Runoff:	**None**
Comments:			

O&M Index:	**3.00**	O&M Quick:	**3100**	O&M Rating:	**3.00**
Structural Index:	**2.00**	Structural Quick:	**2100**	Structural Rating:	**2.00**
Overall Index:	**2.50**	Overall Quick:	**3121**	Overall Rating:	**5.00**

Position	Code	Observation	Video (sec)	Grade
M-707-033				
.0	MGP	General Photo	10	NA
.0	MGP	General Photo	21	NA
2.4	CS	Crack Spiral	38	S 2
2.6	MGP	General Photo	52	NA
4.3	DAZ	Deposits Attached Other	69	M 3
6.0	MGO	General Observation	84	NA



Code: **MGP**
Description: **General Photo**

Distance (ft): **.0**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks:

Code: **MGP**
Description: **General Photo**

Distance (ft): **.0**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks:

Code: **CS**
Description: **Crack Spiral**

Distance (ft): **2.4**
Structural Grade: **2**
O&M Grade: **0**
Clock Start/From: **4**
Clock To: **5**
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks:

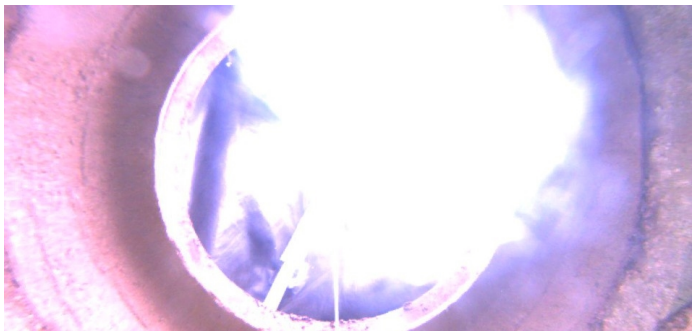

Code: **MGP**
Description: **General Photo**

Distance (ft): **2.6**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks:

Code:	**DAZ**
Description:	**Deposits Attached Other**
Distance (ft):	**4.3**
Structural Grade:	**0**
O&M Grade:	**3**
Clock Start/From:	**12**
Clock To:	**12**
1st Value:	
2nd Value:	
Value Percent:	**15.000**
Step:	**NO**
Remarks:	**Mixed materials**

Code:	**MGO**
Description:	**General Observation**
Distance (ft):	**6.0**
Structural Grade:	**0**
O&M Grade:	**0**
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Step:	**NO**
Remarks:	**Ins. Comp.**
