Manhole Inspection Report

Date:	**05/15/2018**	Weather:		Coding:	**RZMACP**
MH#:	**M-904-034**	Owner:	**NA**	Len. Surveyed:	**5.8**
P.O.#:		Surveyor:	**Jen Costello**	Rim to Invert:	**6.4**
Customer:		Cert. #:	**U-907-5518**	Wall Material:	**Concrete (reinforced)**

Street:	**E. Cleveland Terrace. 877' North of C**	Project:	**Hobart, IN**
City:	**Hobart, IN**	GPS Northing:	**2910904.904**
Location:		GPS Easting:	**2910904.904**
Drain Area:	**Northeast**	GPS Accuracy:	**Sub-Meter**
Cover Shape:	**Circular**	Evidence of Surcharge:	**No**
Cover Size:	**22.5**	Potential for Runoff:	**None**
Comments:			

O&M Index:	**1.50**	O&M Quick:	**2111**	O&M Rating:	**3.00**
Structural Index:	**0.00**	Structural Quick:	**0000**	Structural Rating:	**0.00**
Overall Index:	**1.50**	Overall Quick:	**2111**	Overall Rating:	**3.00**

Position	Code	Observation	Video (sec)	Grade
M-904-034				
.0	MGP	General Photo	10	NA
1.0	MGO	General Observation	25	NA
1.5	MGO	General Observation	40	NA
1.7	VC	Vermin Cockroach	52	M 1
4.3	DSF	Deposits Settled Fine	69	M 2
5.8	MGO	General Observation	83	NA



Code: **MGP**
Description: **General Photo**

Distance (ft): **.0**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks: **ACCESS MH**

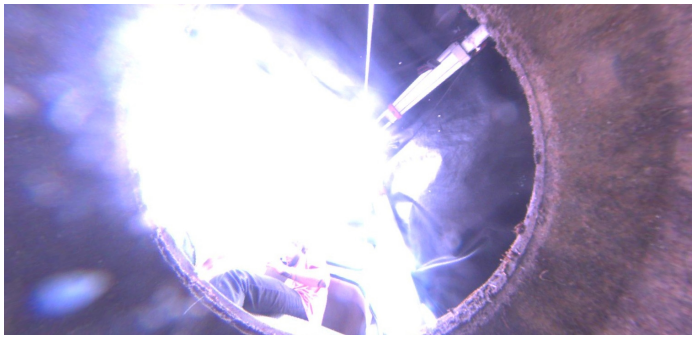

Code: **MGO**
Description: **General Observation**

Distance (ft): **1.0**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks: **UNDERSIDE OF FRAME**

Code: **MGO**
Description: **General Observation**

Distance (ft): **1.5**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks: **BROKEN STEP**

Code: **VC**
Description: **Vermin Cockroach**

Distance (ft): **1.7**
Structural Grade: **0**
O&M Grade: **1**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks:

Code:	**DSF**
Description:	**Deposits Settled Fine**
Distance (ft):	**4.3**
Structural Grade:	**0**
O&M Grade:	**2**
Clock Start/From:	**12**
Clock To:	**6**
1st Value:	
2nd Value:	
Value Percent:	**5.000**
Step:	**NO**
Remarks:	

Code:	**MGO**
Description:	**General Observation**
Distance (ft):	**5.8**
Structural Grade:	**0**
O&M Grade:	**0**
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Step:	**NO**
Remarks:	**END SURVEY**
