Profile/Photo Observation Report

RedZone ROBOTICS

Date:	**04/05/2018**	Weather:		Coding:	**PACP 6.0**
Pipe Length (ft):	**391.8**	Owner:	**NA**	Pre Clean:	**Not Known**
P.O.#:		Surveyor:	**Jen Costello**	PSR:	**P-808-029-030**
Customer:		Clean Date:	**01/01/1900**	Shape:	**C**

Street:	**Hobart**	Flow Control:	**Not Controlled**
City:	**Hobart, IN**	Year Renewed:	
Location:	**Ditch**	Tape/Media #:	
Purpose:	**Maintenance Related**	Dia/Height:	**12"**
Use:	**Sanitary**	Material:	**PVC**
Drain Area:	**NA**	Lining:	**Cured in Place**
Category:	**NA**		
Comment:	**Flow direction wrong.**		
Location Details:		Direction of Survey:	**Upstream**
US MH:	**M-808-030**	DS MH: **M-808-029** Total Length Surveyed (ft):	**16.0**

O&M Index:	**2.00**	O&M Quick:	**2300**	O&M Rating:	**6.00**
Structural Index:	**0.00**	Structural Quick:	**0000**	Structural Rating:	**0.00**
Overall Index:	**2.00**	Overall Quick:	**2300**	Overall Rating:	**6.00**

	Position	Code	Observation	Video (sec)	Grade
M-808-029					
	.0	AMH	Manhole	10	NA
	.0	MWL	Water Level	22	NA
	.0	DAGS(S01)	Deposits Attached Grease	33	M 2
	16.0	DAGS(F01)	Deposits Attached Grease	76	M 2
	16.0	MSA	Abandoned Survey	87	NA

Camera Direction

M-808-030

Code:	**AMH**
Description:	**Manhole**
Distance (ft):	**.0**
Structural Grade:	**0**
O&M Grade:	**0**
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	**NO**
Remarks:	**M-808-029**

Code:	**MWL**
Description:	**Water Level**
Distance (ft):	**.0**
Structural Grade:	**0**
O&M Grade:	**0**
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	**5.000**
Continuous Index:	
Within 8" of Joint:	**NO**
Remarks:	

Code:	**DAGS**
Description:	**Deposits Attached Grease**
Distance (ft):	**.0**
Structural Grade:	**0**
O&M Grade:	**2**
Clock Start/From:	**7**
Clock To:	**5**
1st Value:	
2nd Value:	
Value Percent:	**5.000**
Continuous Index:	**S01**
Within 8" of Joint:	**NO**
Remarks:	
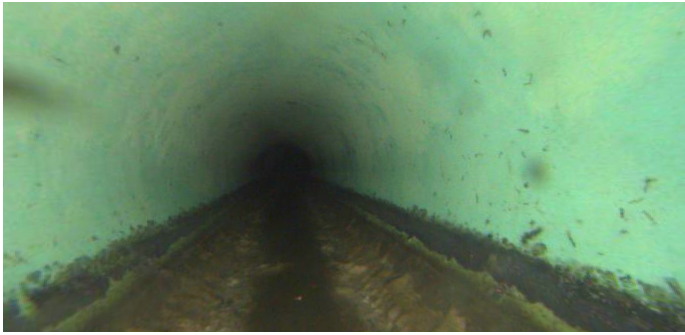
Code: **DAGS**
Description: **Deposits Attached Grease**

Distance (ft): **16.0**
Structural Grade: **0**
O&M Grade: **2**
Clock Start/From: **7**
Clock To: **5**
1st Value:
2nd Value:
Value Percent: **5.000**
Continuous Index: **F01**
Within 8" of Joint: **NO**
Remarks:

Code: **MSA**
Description: **Abandoned Survey**

Distance (ft): **16.0**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Continuous Index:
Within 8" of Joint: **NO**
Remarks: **dags**
